



Monthly Progress Report

July 2022

Lindenhurst Memorial Library



**1 Lee Avenue, Lindenhurst, N.Y.
11757**



Table of Contents

Section I – Work Progress July 2022

Section II – Work Projected for August 2022

Section III – Progress Photos

Section IV – Monthly Workforce Summary



Section I - Work Progress July 2022

- Finished brickwork around exterior of new addition
- Installed dens glass around the exterior of the new addition and North soffit
- Installed cornice around roof of new addition
- Finished roofing on new addition
- Patched in roofing of existing building into new addition
- Landed new addition RTU on roof curb
- Finished framing of walls in new addition
- Roughed in MEPs in new addition ceiling and walls
- Started install of storefront in new addition
- Poured exterior ramp and stairs leading to new addition entrance
- Framed walls of rotunda
- Painted support columns of adult stacks under mezz
- Started installing axiom trim for wood ceiling in adult library
- Whited out ceiling of adult library
- Installed flooring throughout basement and first floor
- Finished install of basement courtyard windows



Section II - Work Planned August 2022

- Phase 1
 - Pour curbs and sidewalks throughout site
 - Rough grade parking lot
 - Begin EIFS install around on North Soffit and new addition
 - Sheetrock walls of new addition
 - Paint ceiling of new addition
 - Install clouds in new addition
 - Install storefront windows and doors in new addition
 - Install folding wall at marriage wall
 - Infill mansard roof of existing building and tie into new addition
 - Start-up mechanical units in phase 1 of existing library
 - Continue install of wood ceilings throughout
 - Finish phase 1 punchlist and turn over adult library on 8/15
 - Begin delivery and set up of casework in phase 1
- Phase 2
 - Abate soffit over 1st floor courtyard windows
 - Demo and replace 1st floor courtyard windows
 - Demo temps divider walls and install plastic dust wall
 - Frame new walls in back offices



Section III – Progress Photos



Masonry, roofing, and cornice installed on new addition



Section III – Progress Photos



Rotunda and North soffit sheathed with densglas



Section III – Progress Photos



New Addition walls framed and MEPs roughed-in




Section III – Progress Photos



Installed flooring throughout basement and 1st Floor (protected) and support columns under mezz painted



Section III – Progress Photos

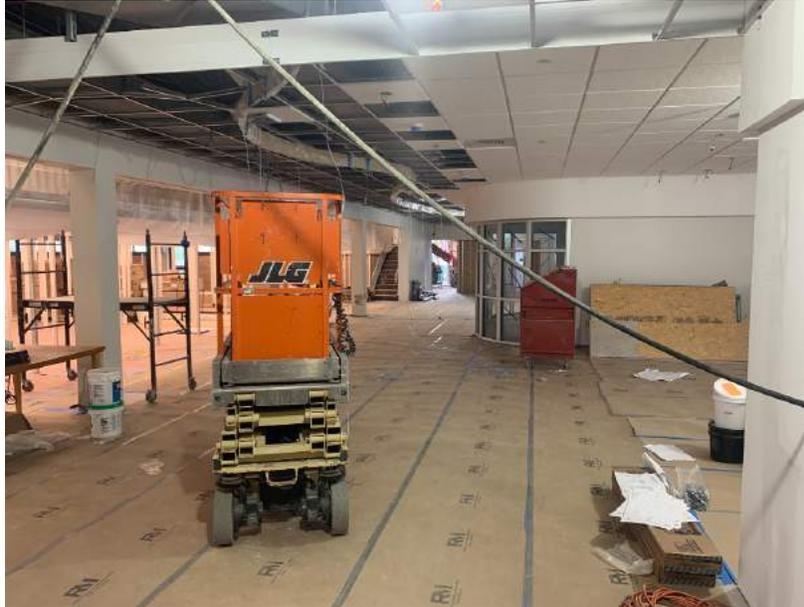


Axiom trim installed and ceiling whited out. All basement courtyard windows installed.
Add Caption



Section IV – Workforce Summary – Company/Hours

July 2022

MANPOWER GRAPH

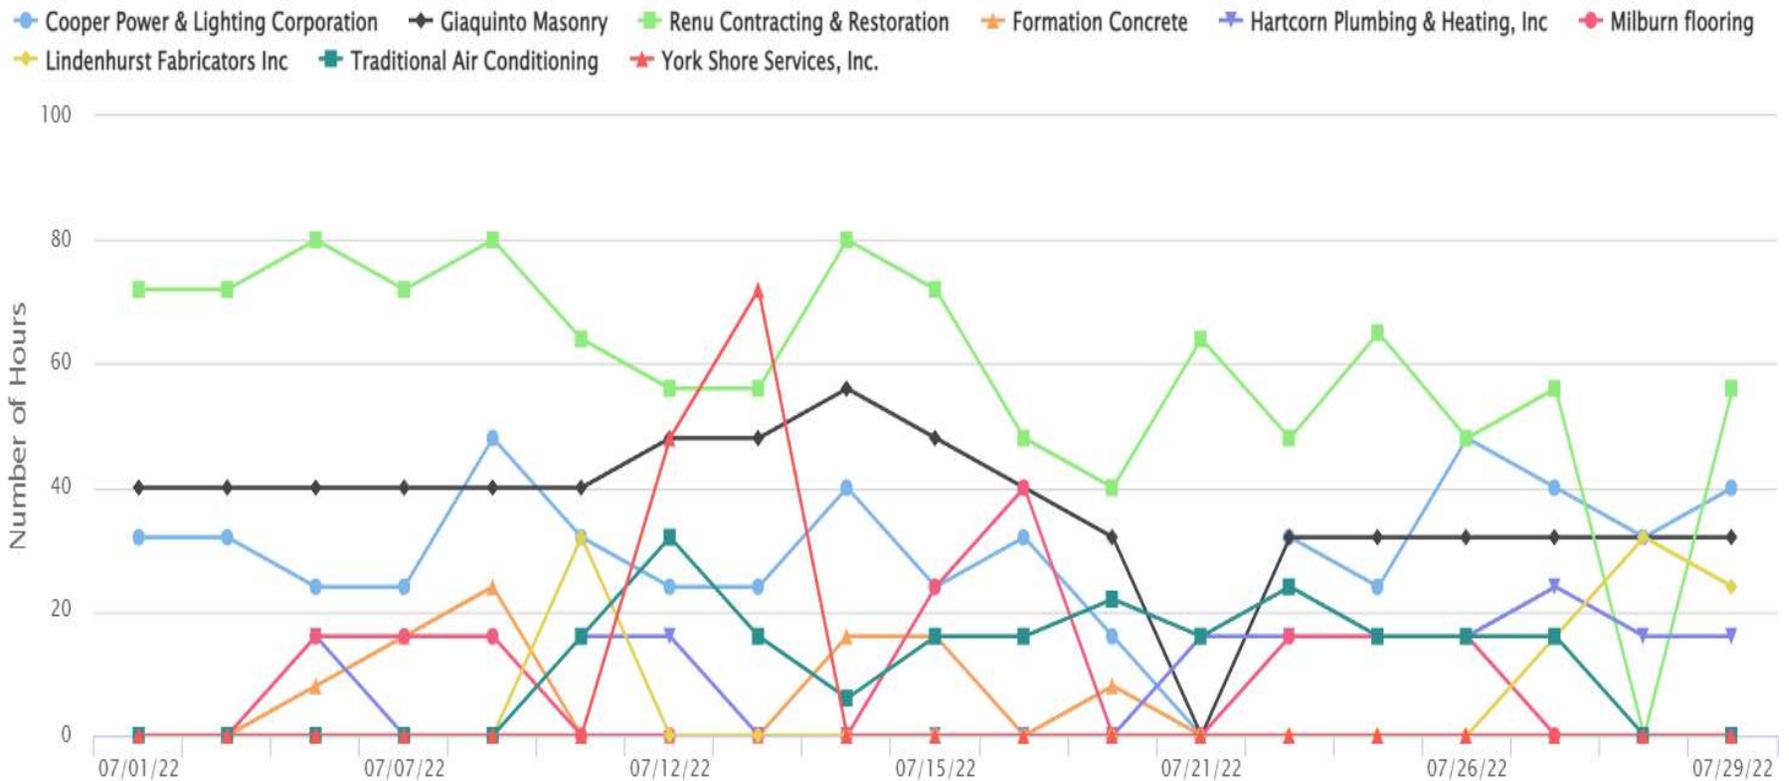



Lindenhurst Memorial Library

July 2022

End of Progress Report
